



Proudly Supported by the NZ Government

New Zealand Government

Te Kāwanatanga o Aotearoa



**NATIONAL
INFRASTRUCTURE**
FUNDING AND FINANCING

CYCLONE RECOVERY REPORT

1 JANUARY TO 30 JUNE 2026





CONTENTS

- CYCLONE RECOVERY OVERVIEW 3
- NIWE & NSW HIGHLIGHTS 4
- NIWE & NSW PROGRAMME TO DATE.....5
- PROGRAMME SUMMARY 6
- CASE STUDY 7
- REGIONAL SUMMARY.....9
- AUCKLAND 10
- HAWKE’S BAY 11
- GISBORNE 12
- NELSON 13
- LOCAL GOVERNMENT FLOOD
RESILIENCE CO-INVESTMENT FUND 14
- HIGHLIGHTS LOCAL GOVERNMENT FLOOD
RESILIENCE CO-INVESTMENT FUND.....15
- LOCAL GOVERNMENT FLOOD
RESILIENCE CO-INVESTMENT FUND 16
- APPROVED PROJECTS 17
- PROJECT PROGRESS 22
- GLOSSARY 24

Dartmoor Bridge rebuild, Hawke’s Bay
Cover: Harania Culvert, Auckland

CYCLONE RECOVERY PROGRAMME

OVERVIEW

NATIONAL INFRASTRUCTURE FUNDING AND FINANCING LIMITED (NIFF) HAS BEEN APPOINTED BY THE GOVERNMENT TO FUND AND OVERSEE THE CYCLONE RECOVERY PROGRAMME.

North Island Weather Events (NIWE)

NIFF is assisting the Crown to provide financial support and project oversight to local councils in regions affected by the North Island Weather Events in January and February 2023. The goal of the NIWE response programme is to reduce intolerable risk to life, ensure insurability of residential properties in affected regions, and re-establish transport links. The NIWE response programme comprises these elements:

- **Category 3 Buyouts** cover the purchase of residential properties that meet the threshold for intolerable risk to life in Auckland, Hawkes Bay, Tairāwhiti, Masterton and Tauranga and where risk from future weather events cannot be mitigated.
- **Category 2 Risk Mitigation** projects look to implement community level or property level measures to reduce the risk of future weather events to Category 2 properties, which are residential properties that meet the threshold for intolerable risk to life where that risk can be mitigated.
- **Regional Transport Projects** cover repairs or replacement of transport infrastructure affected by NIWE events.

Whenua Māori and Marae Pathways

The Crown is currently working with Marae and owners of whenua that is unsafe to occupy as a result of NIWE and has been categorised as Category 3. The Pathway involves the Crown working directly with Marae to provide relocation and rebuild support, and residents to provide relocation support, to ensure they are safe from future severe weather events.

Nelson Severe Weather Event (NSWE)

NIFF is assisting the Crown to provide financial support and programme oversight to Nelson City Council to reduce intolerable risk to life in affected areas via Category 3 Voluntary Buyouts and Category 2 Risk Mitigation Projects.

Local Government Flood Resilience Co-investment Fund (LGFRCIF)

The Local Government Flood Resilience Co-investment Fund provides support to flood resilience projects of several regional and local councils. All councils provide co-funding towards the projects.



ESTIMATED
CATEGORY 3
PROPERTIES

~1,400



ESTIMATED
CATEGORY 2
PROPERTIES

~1,200



CATEGORY 2
RISK MITIGATION
PROJECTS

25



REGIONAL
TRANSPORT
PROJECTS

31



MARAE
PATHWAY

7



FLOOD
RESILIENCE
PROJECTS

35

FUNDING



TOTAL GOVERNMENT
FUNDING

\$1.8bn



TOTAL
CO-FUNDING*

\$1.0bn



TOTAL
PROGRAMME VALUE*

\$2.8bn

* This is an estimated figure and can change as projects require further funding. Includes share of Council funding for Category 3 Properties.

NIWE & NSW HIGHLIGHTS*

FOR THE PERIOD 1 JANUARY TO 30 JUNE 2026

REGIONAL TRANSPORT



APPROVED PROJECTS: 0

Value: \$0m

PROJECTS COMMENCED: 1

Value: \$23m

PROJECTS COMPLETE: 11

Value: \$108m

CATEGORY 2 RISK MITIGATION



APPROVED PROJECTS: 0

Value: \$0m

PROJECTS COMMENCED: 3

Value: \$96m

PROJECTS COMPLETE: 2

Value: \$30m

CATEGORY 3 BUY-OUTS



CATEGORISED PROPERTIES: 0

Value: \$0m

PROPERTIES FUNDED: 123

Value: \$152m

PROPERTIES SETTLED: 111

MARAE REBUILD



APPROVED PROJECTS: 0

Value: \$0m

PROJECTS COMMENCED: 3

Value: \$40m

PROJECTS COMPLETE: 0

Value: \$0m

PROGRAMME OUTCOMES



**BRIDGES /
CULVERTS
COMPLETE**

71



**SLIPS / DROPOUTS
COMPLETE**

240



**STOP BANKS
COMPLETE
(LINEAR METRE)**

3,750



**CATEGORY 2
PROPERTIES
PROTECTED**

26



**MARAE
RELOCATED**

0

FUNDING



**GOVERNMENT
FUNDING APPROVED**

\$2m



**GOVERNMENT
FUNDING INVESTED**

\$167m



**CO-FUNDING
INVESTED**

\$122m



TOTAL INVESTED

\$289m

* Excludes Local Government Flood Resilience Co-investment Fund

NIWE & NSW PROGRAMME TO DATE*

REGIONAL TRANSPORT



APPROVED PROJECTS: 31

Value: \$599m

PROJECTS COMMENCED: 10

32% of Approved Projects

Value: \$291m

49% of Approved Funding

PROJECTS COMPLETE: 19

61% of Approved Projects

Value: \$297m

50% of Approved Funding

CATEGORY 2 RISK MITIGATION



APPROVED PROJECTS: 25

Value: \$581m

PROJECTS COMMENCED: 14

56% of Approved Projects

Value: \$320m

55% of Approved Funding

PROJECTS COMPLETE: 4

16% of Approved Projects

Value: \$31m

5% of Approved Funding

CATEGORY 3 BUY-OUTS



CATEGORISED PROPERTIES: 1,391

Value: \$1,372m

PROPERTIES FUNDED: 1,391

100% of Categorised Properties

Value: \$1,372m

100% of Approved Funding

PROPERTIES SETTLED: 1,367

98% of Categorised Properties

MARAE REBUILD



APPROVED PROJECTS: 7

Value: \$82m

PROJECTS COMMENCED: 6

86% of Approved Projects

Value: \$71m

86% of Approved Funding


PROJECTS COMPLETE: 0

0% of Approved Projects

Value: \$0m

0% of Approved Funding

PROGRAMME OUTCOMES**



BRIDGES / CULVERTS COMPLETE

105

Target 161
65% of target



SLIPS / DROPOUTS COMPLETE

1,721

Target 2,096
82% of target



STOP BANKS COMPLETE (LINEAR METRE)

58,045

Target 78,469
74% of target



CATEGORY 2 PROPERTIES PROTECTED

87

Target ~1,200
7% of target



MARAE RELOCATED

0

Target 7
0% of target

FUNDING



GOVERNMENT FUNDING APPROVED

\$1,733m



GOVERNMENT FUNDING INVESTED

\$1,154m

67% of approved



CO-FUNDING INVESTED

\$827m

85% of approved



TOTAL INVESTED

\$1,979m


73% of approved

* Excludes Local Government Flood Resilience Co-investment Fund.


** Targets may change as project scoping advances.

PROGRAMME SUMMARY

TOTAL FUNDING BY PROGRAMME

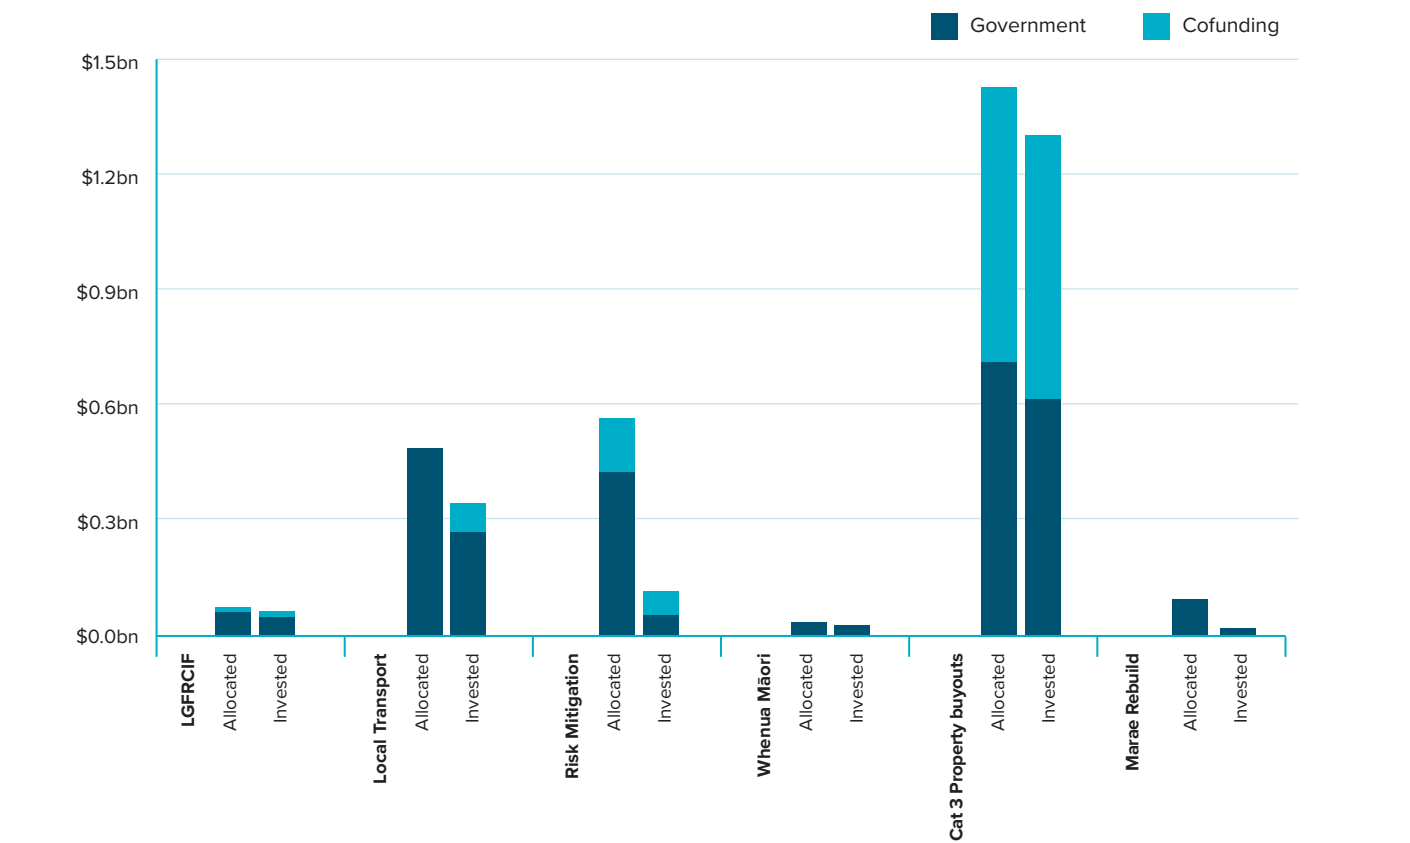

TOTAL FUNDING BY REGION*

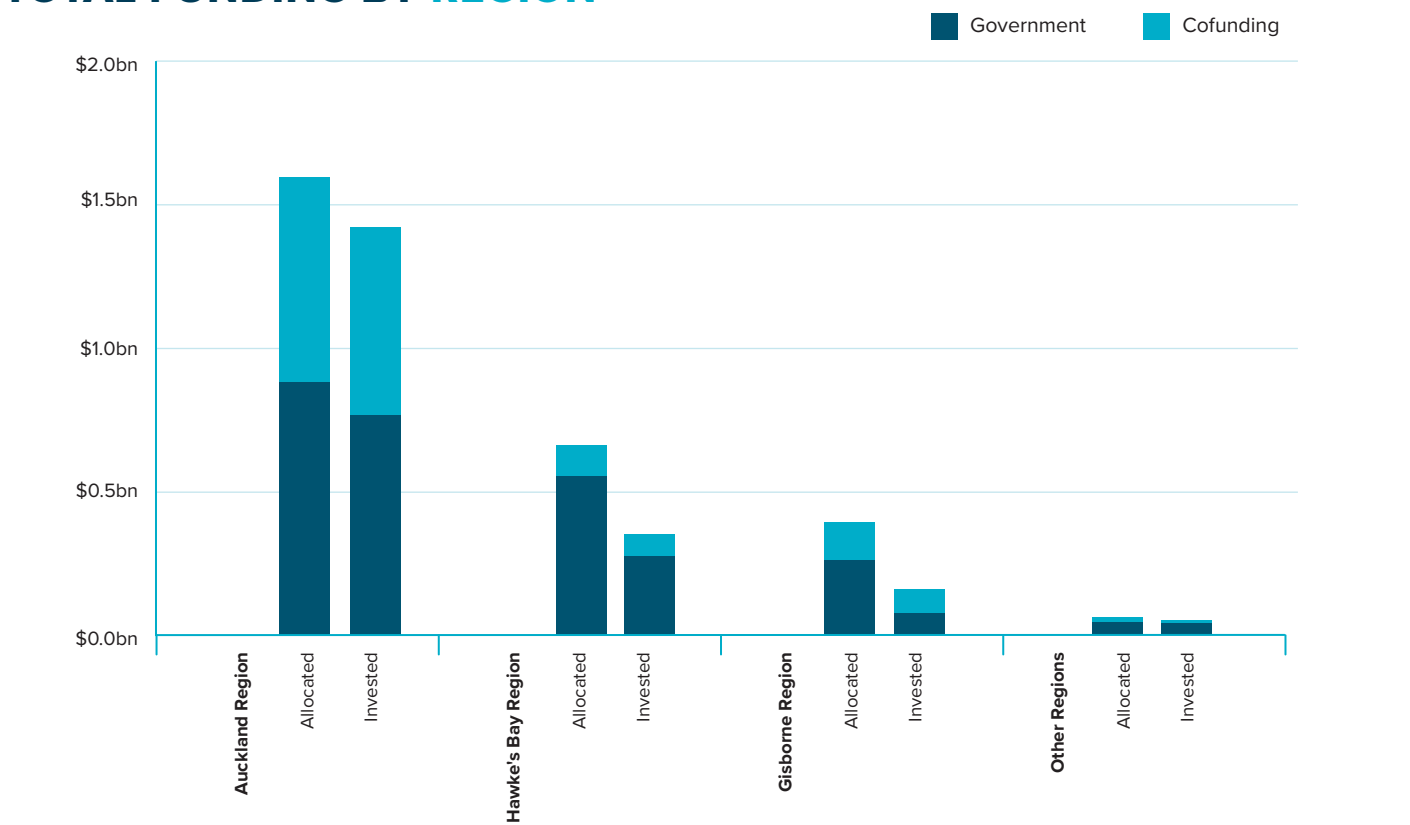

* Excludes Local Government Flood Resilience Co-investment Fund

CASE STUDY

WAIOHIKI FLOOD MITIGATION – HAWKE’S BAY REGIONAL COUNCIL

Govt funding: \$6.76m

Council funding: \$2.24m

Total: \$9.0m

THE IMPACT OF CYCLONE GABRIELLE ON THE WAIOHIKI COMMUNITY

Cyclone Gabrielle caused severe flooding in Hawke’s Bay in February 2023, damaging 92 homes and numerous businesses in the Waiohiki community. Forty-five properties were subsequently classified as Category 2C — an intolerable risk to life in future flood events — under the Government’s land categorisation framework. The scale of the damage highlighted the vulnerability of the Tūtaekurī River catchment and the need for stronger flood protection for Waiohiki and the wider Heretaunga area.

BUILDING FLOOD RESILIENCE

In response, Hawke’s Bay Regional Council delivered a new one kilometre stopbank along the Tūtaekurī River, running from Napier Golf Course to Redclyffe Bridge. The stopbank was designed to provide flood protection against an 1-in-100-year flood event. The project also included reinstating part of the Puketapu Loop cycle trail and diverting the Upokohina Stream onto land formerly used as the golf course’s pitch and putt area.

Construction was completed successfully in May 2026, at a cost of just under \$9m against a \$10m project budget. The project completion was celebrated at a karakia held at



Waiohiki Stopbank Construction



CASE STUDY *Continued...*



Completed Stopbanks

Waiohiki Marae on 22 May, attended by Minister for Local Government Hon Simon Watts, Regional Council Chair Sophie Siers, Ngāi Tahu Ahi representative Alby Grey, and Waiohiki Marae Chair Hinewai Ormsby. As a result of the works, all 45 previously Category 2C properties have been reclassified Category 1, removing risk to life from future flood events at these properties, improving the flood resilience for the Waiohiki community and community confidence.

The completion of the Waiohiki stopbank is a significant milestone in Hawke's Bay's ongoing recovery from Cyclone Gabrielle, delivered through collaboration between central government, Hawke's Bay Regional Council, mana whenua, landowners and the local community. It forms part of the region-wide \$256.5m flood resilience programme extending from Wairoa to Pōrangahau.



REGIONAL TRANSPORT, CATEGORY 2 RISK MITIGATION, AND CATEGORY 3 BUYOUT UPDATE

Puketapu Bridge, Hawke's Bay



AUCKLAND



REGIONAL TRANSPORT



2
PROJECTS
APPROVED
\$112.5m

0
PROJECTS
COMMENCED
\$0.0m

2
PROJECTS
COMPLETE
\$112.5m

CATEGORY 2 RISK MITIGATION



6
PROJECTS
APPROVED
\$230.5m

4
PROJECTS
COMMENCED
\$150.2m

1
PROJECTS
COMPLETE
\$0.3m

PROGRAMME OUTCOMES



BRIDGES / CULVERTS
COMPLETE
2
Target 5
40% Complete



SLIPS / DROPOUTS
COMPLETE
812
Target 812
100% Complete



CATEGORY 2 PROPERTIES
PROTECTED
54
Target 192
28% Complete



RESIDENTIAL PROPERTIES
PROTECTED
0
Target ~1,200
0% Complete



CATEGORY 3
PROPERTIES FUNDED
1,163
Target 1,163
100% Complete

FUNDING



GOVERNMENT
FUNDING APPROVED
\$879.0m



GOVERNMENT
FUNDING INVESTED
\$764.7m
87% of Approved



CO-FUNDING
INVESTED
\$656.5m
92% of Approved



TOTAL
FUNDING INVESTED
\$1,421.2m
89% of Approved



HAWKE'S BAY



NAPIER
CITY COUNCIL
Te Kauhaharo o Ahuriri



**CENTRAL
HAWKE'S BAY**
DISTRICT COUNCIL

**HERETAUNGA
HASTINGS** DISTRICT COUNCIL



REGIONAL TRANSPORT



22
PROJECTS
APPROVED
\$252.6m

4
PROJECTS
COMMENCED
\$60.0m

16
PROJECTS
COMPLETE
\$181.3m

CATEGORY 2 RISK MITIGATION



12
PROJECTS
APPROVED
\$262.3m

9
PROJECTS
COMMENCED
\$152.4m

1
PROJECTS
COMPLETE
\$10.0m

MARAE REBUILD



2
PROJECTS
APPROVED
\$27.6m

1
PROJECTS
COMMENCED
\$16.1m

0
PROJECTS
COMPLETE
\$0.0m

PROGRAMME OUTCOMES



**BRIDGES / CULVERTS
COMPLETE**
7
Target 14
50% Complete



**SLIPS / DROPOUTS
COMPLETE**
639
Target 639
100% Complete



**STOP BANKS COMPLETE
(LINEAR METRE)**
4,045
Target 19,969
20% Complete



**CATEGORY 2 PROPERTIES
PROTECTED**
94
Target 1,089
9% Complete



**CATEGORY 3
PROPERTIES FUNDED**
159
Target 159
100% Complete

FUNDING



**GOVERNMENT
FUNDING APPROVED**
\$551.2m



**GOVERNMENT
FUNDING INVESTED**
\$274.6m
50% of Approved



**CO-FUNDING
INVESTED**
\$76.4m
70% of Approved



**TOTAL
FUNDING INVESTED**
\$351.0m
53% of Approved



GISBORNE/TAIRĀWHITI



Te Kaunihera o Te Tairāwhiti
GISBORNE
DISTRICT COUNCIL

REGIONAL TRANSPORT



7

PROJECTS
APPROVED
\$233.7m

6

PROJECTS
COMMENCED
\$230.7m

1

PROJECTS
COMPLETE
\$3.0m

CATEGORY 2 RISK MITIGATION



5

PROJECTS
APPROVED
\$71.1m

0

PROJECTS
COMMENCED
\$0.0m

1

PROJECTS
COMPLETE
\$20.5m

MARAE REBUILD



5

PROJECTS
APPROVED
\$54.7m

3

PROJECTS
COMMENCED
\$34.0m

0

PROJECTS
COMPLETE
\$0.0m

PROGRAMME OUTCOMES



BRIDGES / CULVERTS
COMPLETE

96

Target 142
68% Complete



STOP BANKS COMPLETE
(LINEAR METRE)

54,000

Target 58,500
92% Complete



CATEGORY 2 PROPERTIES
PROTECTED

0

Target 111
0% Complete



CATEGORY 3
PROPERTIES FUNDED

57

Target 57
100% Complete

FUNDING



GOVERNMENT
FUNDING APPROVED
\$260.1m



GOVERNMENT
FUNDING INVESTED
\$76.0m

29% of Approved



CO-FUNDING
INVESTED
\$81.3m

62% of Approved



TOTAL
FUNDING INVESTED
\$157.3m

40% of Approved



NELSON



CATEGORY 2 RISK MITIGATION



2
PROJECTS APPROVED
\$17.5m

1
PROJECTS COMMENCED
\$17.2m

1
PROJECTS COMPLETE
\$0.3m

PROGRAMME OUTCOMES



SLIPS / DROPOUTS COMPLETE
18
Target 18
100% Complete



CATEGORY 3 PROPERTIES FUNDED
14
Target 14
100% Complete



SLUMP MONITORING
1
Target 1
100% Complete

FUNDING



GOVERNMENT FUNDING APPROVED
\$12.3m



GOVERNMENT FUNDING INVESTED
\$9.5m
77% of Approved



CO-FUNDING INVESTED
\$10.9m
63% of Approved



TOTAL FUNDING INVESTED
\$20.3m
69% of Approved



LOCAL GOVERNMENT FLOOD RESILIENCE CO-INVESTMENT FUND



HIGHLIGHTS LOCAL GOVERNMENT FLOOD RESILIENCE CO-INVESTMENT FUND

FOR THE PERIOD 1 JANUARY TO 30 JUNE 2026

OVERVIEW



PROJECTS COMMENCED

0



PROJECTS COMPLETE

2

INFRASTRUCTURE BUILT



IMPROVED WATERWAYS
(LINEAR METRE)

0m



STOP BANKS
(LINEAR METRE)

0m



CULVERTS

0



PUMP STATIONS
NEW / UPGRADES

0



CATEGORY 2 PROPERTIES
PROTECTED

44

FUNDING



GOVERNMENT
FUNDING INVESTED

\$6m



CO-FUNDING
INVESTED

\$3m



TOTAL
FUNDING INVESTED

\$9m

LOCAL GOVERNMENT FLOOD RESILIENCE CO-INVESTMENT FUND

OVERVIEW



TOTAL PROJECTS

35



PROJECTS COMMENCED

2



PROJECTS COMPLETE

33

INFRASTRUCTURE BUILT



IMPROVED WATERWAYS
(LINEAR METRE)

227,695m



STOP BANKS
(LINEAR METRE)

4,546m



CULVERTS

3



PUMP STATIONS
NEW / UPGRADES

4



CATEGORY 2 PROPERTIES
PROTECTED

121

FUNDING



TOTAL GOVERNMENT
FUNDING

\$63m



TOTAL
CO-FUNDING

\$13m



TOTAL PROGRAMME
VALUE

\$76m



GOVERNMENT
FUNDING INVESTED

\$54m

86% of Total Approved



CO-FUNDING
INVESTED

\$16m

127% of Total Estimated



TOTAL
FUNDING INVESTED

\$70m

93% of Total Approved

APPROVED PROJECTS: JUNE 2026

PROJECT NAME	PROGRAMME	PROJECT STATUS	APPROVED GOVERNMENT FUNDING	APPROVED CO-FUNDING	TOTAL PROJECT VALUE	GOVT INVESTED	TOTAL INVESTED	% INVESTED	WORKS COMMENCEMENT	WORKS COMPLETION
NORTHLAND REGIONAL COUNCIL										
Ngā Manga Atawhai	LGFRClF	Complete	\$2.07m	\$.96m	\$3.03m	\$2.07m	\$3.03m	100.0%	Q1 CY2024	Q2 CY2025
Northland flood intelligence and early warning	LGFRClF	Complete	\$.56m	\$.59m	\$1.15m	\$.56m	\$.91m	79.7%	Q2 CY2024	Q2 CY2025
Northland flood-resilient Maori communities and marae	LGFRClF	Commenced	\$5.24m	\$1.53m	\$6.77m	\$5.14m	\$8.33m	123.2%	Q4 CY2023	Q4 CY2026
Grand Total	3		\$7.87m	\$3.07m	\$10.94m	\$7.77m	\$12.27m	112.2%		
KAIPARA DISTRICT COUNCIL										
Awakino Railway Embankment Stabilisation	LGFRClF	Complete	\$.39m	\$.04m	\$.43m	\$.34m	\$.38m	89.3%	Q4 CY2024	Q3 CY2025
Awakino river mouth cleaning	LGFRClF	Complete	\$.35m	\$.20m	\$.55m	\$.11m	\$.21m	38.8%	Q2 CY2024	Q4 CY2025
Beach Road culvert	LGFRClF	Complete	\$.40m	\$.05m	\$.45m	\$.40m	\$.45m	100.0%	Q4 CY2025	Q1 CY2026
Dargaville Stop Bank Repairs	LGFRClF	Complete	\$.50m	\$.04m	\$.54m	\$.50m	\$.67m	123.6%	Q2 CY2024	Q3 CY2025
Dargaville Wastewater Treatment Plant Pond Heightening	LGFRClF	Complete	\$.65m	\$.04m	\$.69m	\$.65m	\$.69m	100.0%	Q3 CY2025	Q4 CY2025
Murphy Bower Stopbank	LGFRClF	Complete	\$.28m	\$.59m	\$.87m	\$.28m	\$1.31m	150.0%	Q1 CY2024	Q2 CY2024
Robert Street Stormwater	LGFRClF	Complete	\$.50m	\$.04m	\$.54m	\$.43m	\$.47m	87.6%	Q2 CY2024	Q2 CY2024
Grand Total	7		\$3.07m	\$1.00m	\$4.07m	\$2.72m	\$4.18m	102.8%		
WHANGĀREI DISTRICT COUNCIL										
Morningside Flood Relief Project	LGFRClF	Complete	\$3.00m	\$.50m	\$3.50m	\$3.00m	\$4.04m	115.5%	Q1 CY2025	Q2 CY2025
Grand Total	1		\$3.00m	\$.50m	\$3.50m	\$3.00m	\$4.04m	115.5%		
AUCKLAND COUNCIL										
Cat 3 Property Buyouts	Cat 3 Property buyouts	Commenced	\$626.05m	\$626.05m	\$1252.10m	\$626.05m	\$1252.10m	100.0%	Q4 CY2023	Q4 CY2025
Accelerating Aucklanders storm readiness	LGFRClF	Complete	\$2.00m	\$.00m	\$2.00m	\$1.97m	\$1.97m	98.7%	Q2 CY2024	Q4 CY2025
Mill Flat Road Bridge and Manukau Heads Road	Local Transport	Complete	\$15.21m	\$2.50m	\$17.71m	\$10.38m	\$10.38m	58.6%	Q4 CY2024	Q2 CY2026
Road Network Reinstatement Programme	Local Transport	Complete	\$94.79m	\$.00m	\$94.79m	\$94.79m	\$94.79m	100.0%	Q2 CY2023	Q4 CY2025
Category 2P properties region wide locations	Risk Mitigation	Commenced	\$24.04m	\$14.73m	\$38.78m	\$8.10m	\$16.22m	41.8%	Q3 CY2024	Q2 CY2027
Clover Drive	Risk Mitigation	In Prework	\$49.60m	\$30.40m	\$80.00m	\$6.56m	\$13.74m	17.2%	Q4 CY2027	Q4 CY2029
Harania, Mangere - Flood Risk Resilience	Risk Mitigation	Commenced	\$18.15m	\$11.13m	\$29.28m	\$7.25m	\$13.30m	45.4%	Q2 CY2025	Q4 CY2026
Muriwai Landslip and Stormwater Resilience - Domain Crescent	Risk Mitigation	Discontinued	\$.16m	\$.10m	\$.25m	\$.16m	\$.16m	61.9%	Q4 CY2024	Q4 CY2024
Te Ararata, Mangere - Flood Risk Resilience	Risk Mitigation	Commenced	\$14.93m	\$9.15m	\$24.08m	\$9.41m	\$17.71m	73.6%	Q2 CY2025	Q3 CY2026
Wairau	Risk Mitigation	Commenced	\$36.03m	\$22.08m	\$58.10m	\$2.01m	\$2.82m	4.9%	Q4 CY2025	Q3 CY2030
Grand Total	10		\$880.96m	\$716.14m	\$1597.10m	\$766.69m	\$1423.20m	89.1%		

continued on next page

APPROVED PROJECTS: JUNE 2026

PROJECT NAME	PROGRAMME	PROJECT STATUS	APPROVED GOVERNMENT FUNDING	APPROVED CO-FUNDING	TOTAL PROJECT VALUE	GOVT INVESTED	TOTAL INVESTED	% INVESTED	WORKS COMMENCEMENT	WORKS COMPLETION
WAIKATO REGIONAL COUNCIL										
Coromandel River(s) Resilience Initiative	LGFRCIF	Complete	\$.71m	\$.66m	\$1.37m	\$.71m	\$1.41m	103.0%	Q4 CY2023	Q2 CY2025
Coromandel Storm damaged tree removal	LGFRCIF	Complete	\$.64m	\$.28m	\$.92m	\$.64m	\$.87m	94.7%	Q1 CY2024	Q2 CY2025
Grahams Creek Flood Scheme Enhancement	LGFRCIF	Complete	\$.33m	\$.04m	\$.37m	\$.33m	\$.42m	112.4%	Q1 CY2025	Q1 CY2025
Waihou and Piako Rivers Network Recovery	LGFRCIF	Complete	\$.94m	\$.32m	\$1.26m	\$.94m	\$1.26m	100.0%	Q3 CY2023	Q2 CY2024
Waikato, Waipā and West Coast Rivers	LGFRCIF	Complete	\$.70m	\$1.05m	\$1.75m	\$.70m	\$1.76m	100.2%	Q4 CY2023	Q2 CY2025
Grand Total	5		\$3.33m	\$2.35m	\$5.67m	\$3.33m	\$5.71m	100.7%		
THAMES-COROMANDEL DISTRICT COUNCIL										
Thornton Bay slip stabilisation	LGFRCIF	Complete	\$1.30m	\$.15m	\$1.45m	\$1.27m	\$1.42m	97.7%	Q1 CY2025	Q2 CY2025
Grand Total	1		\$1.30m	\$.15m	\$1.45m	\$1.27m	\$1.42m	97.7%		
WAIKATO DISTRICT COUNCIL										
Homeowner support in mitigating risks from North Island Weather Events	LGFRCIF	Complete	\$1.10m	\$.39m	\$1.49m	\$1.10m	\$1.64m	110.0%	Q3 CY2025	Q2 CY2026
Lake Hakanoa Three-Waters resilience work	LGFRCIF	Complete	\$.98m	\$.89m	\$1.87m	\$.98m	\$1.98m	105.9%	Q2 CY2025	Q3 CY2025
Port Waikato Three-Waters Resilience Work	LGFRCIF	Complete	\$2.35m	\$.50m	\$2.85m	\$2.35m	\$3.15m	110.5%	Q1 CY2025	Q3 CY2025
Grand Total	3		\$4.43m	\$1.78m	\$6.21m	\$4.43m	\$6.77m	109.0%		
TAURANGA CITY COUNCIL										
Category 3 Tauranga	Cat 3 Property buyouts	Complete	\$.90m	\$.90m	\$1.80m	\$.90m	\$1.80m	100.0%	Q3 CY2024	Q4 CY2025
Egret Avenue and Te Mutu Crescent land slips	LGFRCIF	Complete	\$2.85m	\$.00m	\$2.85m	\$2.85m	\$2.85m	100.0%	Q4 CY2024	Q3 CY2025
Grand Total	2		\$3.75m	\$.90m	\$4.65m	\$3.75m	\$3.75m	80.7%		
GISBORNE DISTRICT COUNCIL										
Cat 3 Property Buyouts	Cat 3 Property buyouts	Commenced	\$16.34m	\$16.34m	\$32.68m	\$16.29m	\$32.59m	99.7%	Q1 CY2024	Q2 CY2025
Category2P - Mitigation Tairāwhiti	LGFRCIF	Commenced	\$10.74m	\$.26m	\$11.00m	\$7.01m	\$7.24m	65.8%	Q2 CY2023	Q4 CY2026
Tairāwhiti Enhanced Flood Intelligence and Resilience	LGFRCIF	Complete	\$1.20m	\$.25m	\$1.45m	\$1.20m	\$1.45m	99.7%	Q1 CY2024	Q4 CY2025
Black Bridges	Local Transport	Commenced	\$12.78m	\$57.67m	\$70.45m	\$.00m	\$18.90m	26.8%	Q3 CY2023	Q4 CY2027
Build Capacity	Local Transport	Complete	\$3.00m	\$.00m	\$3.00m	\$1.48m	\$1.48m	49.3%	Q2 CY2024	Q2 CY2026
Community Roading Improvements	Local Transport	Commenced	\$36.88m	\$.00m	\$36.88m	\$10.67m	\$10.67m	28.9%	Q1 CY2025	Q2 CY2027
Green Bridges	Local Transport	Commenced	\$1.00m	\$.00m	\$1.00m	\$.78m	\$.78m	78.1%	Q3 CY2023	Q2 CY2026
Red/Orange Bridges	Local Transport	Commenced	\$15.00m	\$9.92m	\$24.92m	\$5.80m	\$20.81m	83.5%	Q1 CY2024	Q4 CY2027
Slips and Dropouts	Local Transport	Commenced	\$11.34m	\$41.16m	\$52.50m	\$3.15m	\$30.44m	58.0%	Q4 CY2024	Q2 CY2027
Tiniroto Road	Local Transport	Commenced	\$45.00m	\$.00m	\$45.00m	\$6.72m	\$6.72m	14.9%	Q1 CY2024	Q4 CY2027

continued on next page

APPROVED PROJECTS: JUNE 2026

PROJECT NAME	PROGRAMME	PROJECT STATUS	APPROVED GOVERNMENT FUNDING	APPROVED CO-FUNDING	TOTAL PROJECT VALUE	GOVT INVESTED	TOTAL INVESTED	% INVESTED	WORKS COMMENCEMENT	WORKS COMPLETION
East Coast Flood Resilience Improvements	Risk Mitigation	In Prework	\$19.08m	\$2.12m	\$21.20m	\$1.30m	\$1.53m	7.2%	Q3 CY2027	Q4 CY2030
Gisborne City Flood Resilience Improvements	Risk Mitigation	In Prework	\$13.54m	\$1.50m	\$15.04m	\$0.63m	\$0.76m	5.0%	Q4 CY2026	Q3 CY2028
Te Arai Flood Resilience Improvements	Risk Mitigation	In Prework	\$1.08m	\$0.12m	\$1.20m	\$0.00m	\$0.05m	4.1%	Q2 CY2026	Q2 CY2027
Te Karaka Flood Resilience Improvements	Risk Mitigation	In Prework	\$11.88m	\$1.32m	\$13.20m	\$0.78m	\$0.96m	7.2%	Q4 CY2026	Q4 CY2028
Waipaoa River Flood Control Scheme/Waipaoa Stopbanks	Risk Mitigation	Complete	\$18.41m	\$2.05m	\$20.46m	\$16.35m	\$19.56m	95.6%	Q4 CY2023	Q2 CY2026
Grand Total	15		\$217.27m	\$132.71m	\$349.98m	\$72.15m	\$153.92m	44.0%		

TOITU TAIRĀWHITI BUILTSMART LTD										
Raising Tairāwhiti	LGFRCIF	Complete	\$5.28m	\$0.00m	\$5.28m	\$5.06m	\$5.06m	95.8%	Q2 CY2024	Q2 CY2026
Grand Total	1		\$5.28m	\$0.00m	\$5.28m	\$5.06m	\$5.06m	95.8%		

HAWKE'S BAY REGIONAL COUNCIL										
Havelock North Mangarau Stream 2C Upgrade	Risk Mitigation	Commenced	\$7.52m	\$2.49m	\$10.00m	\$1.56m	\$3.32m	33.2%	Q4 CY2024	Q4 CY2026
Omahu / Ohiti Road Flood Management Scheme	Risk Mitigation	Commenced	\$7.52m	\$2.49m	\$10.00m	\$5.62m	\$7.86m	78.6%	Q1 CY2025	Q3 CY2026
Pakowhai	Risk Mitigation	Commenced	\$37.58m	\$12.43m	\$50.00m	\$10.73m	\$15.84m	31.7%	Q2 CY2026	Q2 CY2027
Porongahau	Risk Mitigation	Commenced	\$10.52m	\$4.07m	\$14.59m	\$1.03m	\$3.13m	21.4%	Q2 CY2026	Q4 CY2026
Pump Stations	Risk Mitigation	Commenced	\$23.56m	\$7.79m	\$31.35m	\$3.68m	\$5.44m	17.4%	Q2 CY2026	Q3 CY2027
Rapid Repair LoS Additional Work	Risk Mitigation	In Prework	\$22.51m	\$7.44m	\$29.96m	\$0.00m	\$0.62m	2.1%	Q3 CY2026	Q1 CY2027
Scheme reviews	Risk Mitigation	Commenced	\$2.25m	\$1.73m	\$3.99m	\$1.45m	\$3.18m	79.8%	Q4 CY2024	Q3 CY2026
Telemetry Upgrade	Risk Mitigation	Commenced	\$2.75m	\$0.91m	\$3.65m	\$1.59m	\$2.23m	61.0%	Q3 CY2024	Q4 CY2026
Waiohiki Flood Mitigation	Risk Mitigation	Complete	\$7.52m	\$2.49m	\$10.00m	\$4.66m	\$6.74m	67.4%	Q4 CY2024	Q2 CY2026
Wairoa	Risk Mitigation	In Prework	\$70.00m	\$0.00m	\$70.00m	\$9.99m	\$9.99m	14.3%	Q2 CY2026	Q2 CY2027
Whirinaki Flood Management Scheme	Risk Mitigation	Commenced	\$17.33m	\$5.73m	\$23.06m	\$6.62m	\$9.39m	40.7%	Q4 CY2025	Q4 CY2026
Grand Total	11		\$209.04m	\$47.55m	\$256.59m	\$46.93m	\$67.74m	26.4%		

WAIROA DISTRICT COUNCIL										
Bridge 131- Te Reinga Bridge Replacement	Local Transport	Complete	\$14.00m	\$0.00m	\$14.00m	\$13.12m	\$13.12m	93.7%	Q2 CY2025	Q2 CY2026
Grand Total	1		\$14.00m	\$0.00m	\$14.00m	\$13.12m	\$13.12m	93.7%		

APPROVED PROJECTS: JUNE 2026


PROJECT NAME	PROGRAMME	PROJECT STATUS	APPROVED GOVERNMENT FUNDING	APPROVED CO-FUNDING	TOTAL PROJECT VALUE	GOVT INVESTED	TOTAL INVESTED	% INVESTED	WORKS COMMENCEMENT	WORKS COMPLETION
HASTINGS DISTRICT COUNCIL										
Cat 3 Property Buyouts	Cat 3 Property buyouts	Complete	\$53.50m	\$53.50m	\$107.00m	\$37.71m	\$75.42m	70.5%	Q4 CY2023	Q2 CY2025
Aropaoanui Low Level Bridge Rebuild	Local Transport	In Prework	\$3.42m	\$0.00m	\$3.42m	\$0.59m	\$0.59m	17.2%	Q4 CY2026	Q1 CY2027
Chrystal Twin Culvert	Local Transport	Complete	\$3.50m	\$0.00m	\$3.50m	\$3.31m	\$3.31m	94.4%	Q2 CY2024	Q3 CY2024
Cyclone Road renewals	Local Transport	Complete	\$12.42m	\$0.00m	\$12.42m	\$7.91m	\$7.91m	63.7%	Q4 CY2024	Q2 CY2026
Dartmoor Bridge Rebuild	Local Transport	Commenced	\$22.50m	\$0.00m	\$22.50m	\$4.11m	\$4.11m	18.3%	Q1 CY2026	Q4 CY2026
Dartmoor Road Slips	Local Transport	Complete	\$25.53m	\$0.00m	\$25.53m	\$19.16m	\$19.16m	75.0%	Q1 CY2024	Q1 CY2026
Glengarry Road Slips	Local Transport	Complete	\$4.60m	\$0.00m	\$4.60m	\$4.05m	\$4.05m	88.0%	Q3 CY2024	Q1 CY2025
Kahika Road Culvert	Local Transport	Commenced	\$1.48m	\$0.00m	\$1.48m	\$0.99m	\$0.99m	66.6%	Q3 CY2024	Q4 CY2026
Kahuranaki Road Slip	Local Transport	Complete	\$2.00m	\$0.00m	\$2.00m	\$1.20m	\$1.20m	59.9%	Q1 CY2025	Q1 CY2026
Kereru Road 3rd Gorge Culvert	Local Transport	Complete	\$29.55m	\$0.00m	\$29.55m	\$29.33m	\$29.33m	99.3%	Q1 CY2024	Q2 CY2025
Kereru Road Slips	Local Transport	Complete	\$3.54m	\$0.00m	\$3.54m	\$3.04m	\$3.04m	85.8%	Q3 CY2024	Q1 CY2026
Matapiro Bridge Replacement	Local Transport	Complete	\$6.87m	\$0.00m	\$6.87m	\$4.33m	\$4.33m	63.1%	Q3 CY2024	Q2 CY2025
McVicar's Culvert Rebuild	Local Transport	Complete	\$3.66m	\$0.00m	\$3.66m	\$2.15m	\$2.15m	58.9%	Q1 CY2025	Q1 CY2026
Puketapu Bridge 245 Rebuild	Local Transport	Complete	\$28.00m	\$0.00m	\$28.00m	\$26.87m	\$26.87m	96.0%	Q2 CY2024	Q3 CY2025
Puketitiri Road Tier 2 and 3 Slips	Local Transport	Complete	\$10.00m	\$0.00m	\$10.00m	\$9.40m	\$9.40m	94.0%	Q4 CY2024	Q2 CY2026
Rissington Bridge Replacement	Local Transport	Commenced	\$25.00m	\$0.00m	\$25.00m	\$6.92m	\$6.92m	27.7%	Q3 CY2025	Q3 CY2026
Slips Tier 0 and 1	Local Transport	Complete	\$20.00m	\$0.00m	\$20.00m	\$20.00m	\$32.00m	160.0%	Q3 CY2023	Q3 CY2023
Taihapa Road Slips	Local Transport	Complete	\$8.65m	\$0.00m	\$8.65m	\$7.08m	\$7.08m	81.8%	Q3 CY2024	Q2 CY2026
Waihau Road Slips	Local Transport	Complete	\$7.23m	\$0.00m	\$7.23m	\$3.00m	\$3.00m	41.5%	Q2 CY2025	Q2 CY2026
Waimarama Road Slip	Local Transport	Complete	\$1.79m	\$0.00m	\$1.79m	\$0.88m	\$0.88m	49.2%	Q1 CY2025	Q2 CY2025
Whanawhana Bridge	Local Transport	In Prework	\$7.87m	\$0.00m	\$7.87m	\$0.85m	\$0.85m	10.8%	Q3 CY2026	Q2 CY2027
Grand Total	21		\$281.09m	\$53.50m	\$334.59m	\$192.88m	\$242.59m	72.5%		
NAPIER CITY COUNCIL										
Cat 3 Property buyouts Napier City	Cat 3 Property buyouts	Complete	\$5.00m	\$5.00m	\$10.00m	\$3.91m	\$7.81m	78.1%	Q4 CY2023	Q2 CY2025
Grand Total	1		\$5.00m	\$5.00m	\$10.00m	\$3.91m	\$7.81m	78.1%		
CENTRAL HAWKE'S BAY DISTRICT COUNCIL										
Stop bank to protect the Waipawa Drinking Water Treatment Plant	LGFRCIF	Complete	\$0.60m	\$0.00m	\$0.60m	\$0.57m	\$0.57m	94.9%	Q1 CY2024	Q2 CY2024
4 Regional Transport Projects	Local Transport	Commenced	\$11.00m	\$0.00m	\$11.00m	\$7.64m	\$7.64m	69.5%	Q4 CY2023	Q2 CY2027
Relocate Waipawa Water Treatment Plant	Risk Mitigation	Commenced	\$3.46m	\$2.29m	\$5.75m	\$2.20m	\$4.13m	71.8%	Q1 CY2025	Q3 CY2026
Grand Total	3		\$15.06m	\$2.29m	\$17.35m	\$10.41m	\$12.34m	71.1%		

continued on next page

APPROVED PROJECTS: JUNE 2026

PROJECT NAME	PROGRAMME	PROJECT STATUS	APPROVED GOVERNMENT FUNDING	APPROVED CO-FUNDING	TOTAL PROJECT VALUE	GOVT INVESTED	TOTAL INVESTED	% INVESTED	WORKS COMMENCEMENT	WORKS COMPLETION
HORIZON REGIONAL COUNCIL										
Flood forecasting & communication resilience upgrades in Horizons Region	LGFRCIF	Complete	\$3.65m	\$1.34m	\$4.99m	\$3.65m	\$4.72m	94.6%	Q3 CY2023	Q3 CY2025
Reducing risks to people and houses in the Pohangina Catchment	LGFRCIF	Complete	\$.33m	\$.56m	\$.88m	\$.33m	\$.77m	87.4%	Q3 CY2023	Q1 CY2025
Grand Total	2		\$3.97m	\$1.90m	\$5.87m	\$3.97m	\$5.49m	93.5%		
MANAWATŪ DISTRICT COUNCIL										
Stanway-Halcombe water supply upgrade	LGFRCIF	Complete	\$1.68m	\$.98m	\$2.65m	\$1.68m	\$3.29m	124.2%	Q3 CY2024	Q2 CY2025
Grand Total	1		\$1.68m	\$.98m	\$2.65m	\$1.68m	\$3.29m	124.2%		
GREATER WELLINGTON REGIONAL COUNCIL										
Eastern Wairarapa Early Flood warning systems upgrade	LGFRCIF	Complete	\$.90m	\$.10m	\$1.00m	\$.82m	\$.91m	90.6%	Q3 CY2024	Q4 CY2025
Wairarapa Recovery and Flooding Resilience Works	LGFRCIF	Complete	\$3.50m	\$.25m	\$3.75m	\$3.50m	\$3.75m	99.9%	Q1 CY2024	Q4 CY2024
Grand Total	2		\$4.40m	\$.35m	\$4.75m	\$4.31m	\$4.65m	97.9%		
MASTERTON DISTRICT COUNCIL										
Masterton Category 3	Cat 3 Property buyouts	Complete	\$1.35m	\$1.35m	\$2.71m	\$1.12m	\$2.24m	82.8%	Q4 CY2024	Q2 CY2025
Cockburn St Sewer Resilience	LGFRCIF	Complete	\$1.30m	\$.20m	\$1.50m	\$1.30m	\$1.68m	111.7%	Q2 CY2024	Q2 CY2025
Flood relocation Wairarapa	LGFRCIF	Complete	\$4.80m	\$.00m	\$4.80m	\$.80m	\$.80m	16.7%	Q2 CY2024	Q2 CY2025
Riversdale water protection	LGFRCIF	Complete	\$.41m	\$.04m	\$.45m	\$.38m	\$.42m	93.2%	Q2 CY2025	Q2 CY2025
Grand Total	4		\$7.87m	\$1.59m	\$9.46m	\$3.60m	\$4.02m	42.5%		
CARTERTON DISTRICT COUNCIL										
Flat Point Flood Resilience	LGFRCIF	Complete	\$.35m	\$.06m	\$.41m	\$.32m	\$.38m	93.4%	Q1 CY2025	Q2 CY2025
Grand Total	1		\$.35m	\$.06m	\$.41m	\$.32m	\$.38m	93.4%		
NELSON CITY COUNCIL										
Cat 3 Property buyouts Nelson City Council	Cat 3 Property buyouts	Complete	\$6.00m	\$6.00m	\$12.00m	\$4.82m	\$9.64m	80.4%	Q3 CY2024	Q2 CY2025
Risk Mitigation Projects	Risk Mitigation	Commenced	\$6.00m	\$11.19m	\$17.19m	\$4.33m	\$10.40m	60.5%	Q1 CY2024	Q2 CY2026
Tāhunanui Slump Monitoring	Risk Mitigation	Complete	\$.30m	\$.00m	\$.30m	\$.30m	\$.30m	100.0%	Q1 CY2024	Q4 CY2024
Grand Total	3		\$12.30m	\$17.19m	\$29.49m	\$9.45m	\$20.35m	69.0%		
Grand Total	98		\$1685.01m	\$989.00m	\$2674.01m	\$1160.73m	\$2002.10m	74.9%		

PROJECT PROGRESS

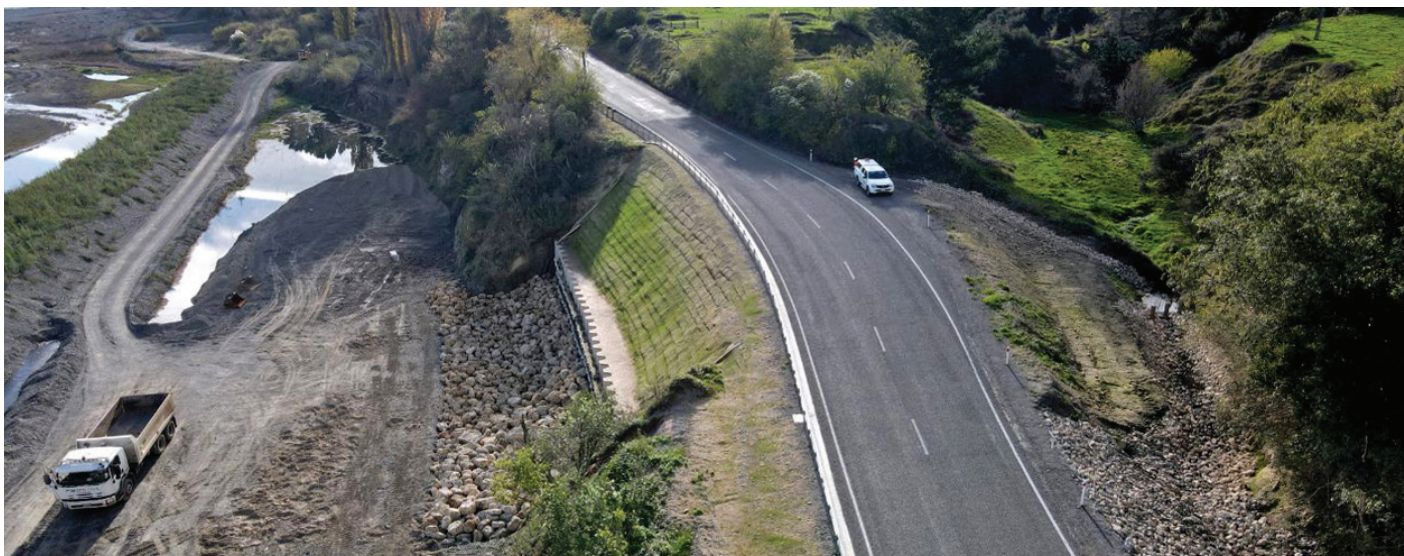

Dartmoor Road Slips, Hawke's Bay



Hinemaurea Marae Rebuild, Gisborne



Rangatira Marae Rebuild, Gisborne



Telemetry Upgrades, Hawke's Bay



Ohiti (Omahu) Stopbanks, Hawke's Bay



Pekapeka Rissington Bridge, Hawke's Bay



Te Ararata Creek Flood Resilience, Auckland

GLOSSARY

PROJECT DEFINITIONS:

Approved: The project has been approved by Cyclone Recovery Unit (CRU) and the Ministers for funding to be released to Councils.

Projects Commenced: refers to projects that have commenced the construction or implementation phase. The project is now actively being built or put into action.

Procurement: The total value of procurement and supply contracts committed to by the Councils.

PROPERTY CATEGORY DEFINITIONS:

Category 3: properties affected by the NIWE or NSWE event where future severe weather event risk cannot be sufficiently mitigated. In some cases some current land use may remain acceptable, while for others there is an intolerable risk of injury or death.

Category 2C: properties affected by the NIWE or NSWE event where community level interventions are effective in managing future severe weather events risk.

Category 2P: properties affected by the NIWE or NSWE event where property level interventions are needed to manage future severe weather event risk, including in tandem with community level interventions.

FUNDING DEFINITIONS:

Government Funding: Financial support provided by the government to Councils to support Cyclone Recovery projects and initiatives.

Co-Funding: Financial support provided by Council sources to fund Cyclone Recovery projects and initiatives.

Government Funding Invested: The value of financial support the Government has contributed and paid to Councils for Cyclone Recovery projects.

Co-Funding Invested: The value of financial support the Council has contributed and paid for Cyclone Recovery projects.
